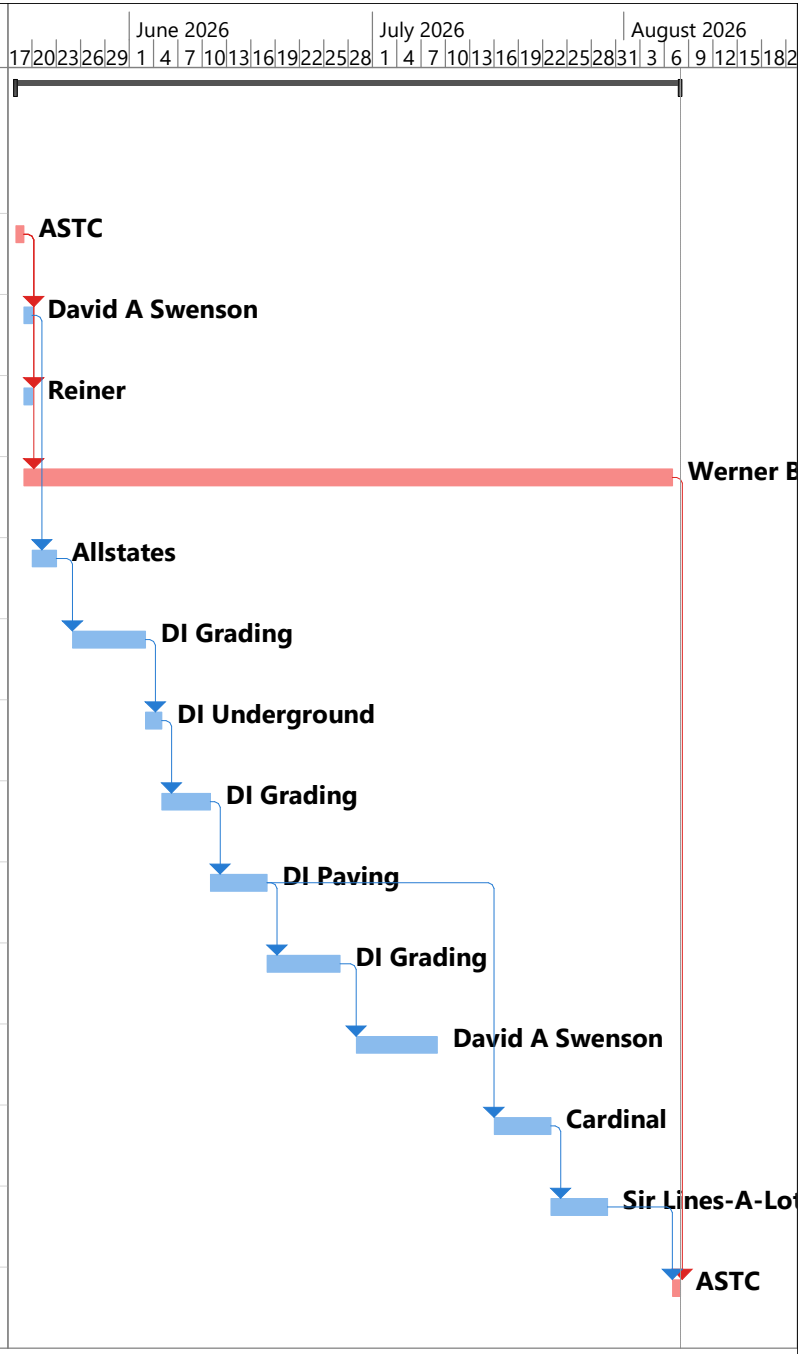ID	Task Name	Duration	Start	Finish	Predecessors
1	**Redwood Falls Municipal Airport Runway 12/30 Rehabilitation**	**60 days**	**Mon 5/18/26**	**Fri 8/7/26**	
2	Temporary Traffic Control	1 day	Mon 5/18/26	Mon 5/18/26	
3	Initial Erosion Control	1 day	Tue 5/19/26	Tue 5/19/26	2
4	Saw Cutting	1 day	Tue 5/19/26	Tue 5/19/26	2
5	Electrical	58 days	Tue 5/19/26	Thu 8/6/26	2
6	Milling	3 days	Wed 5/20/26	Fri 5/22/26	3
7	Common Ex/Embankment	7 days	Mon 5/25/26	Tue 6/2/26	6
8	Pipework	2 days	Wed 6/3/26	Thu 6/4/26	7
9	Class 5/Select Granular	4 days	Fri 6/5/26	Wed 6/10/26	8
10	Paving	5 days	Thu 6/11/26	Wed 6/17/26	9
11	Topsoil Respread	7 days	Thu 6/18/26	Fri 6/26/26	10
12	Seeding/Mulching	8 days	Mon 6/29/26	Wed 7/8/26	11
13	Pavement Grooving	5 days	Thu 7/16/26	Wed 7/22/26	10FS+20 days
14	Pavement Markings	5 days	Thu 7/23/26	Wed 7/29/26	13
15	Remove Traffic Control	1 day	Fri 8/7/26	Fri 8/7/26	14,5
